

Phone 877-942-5613

158490
09/17/2016
Hamlin Roofing Services, Inc.
Advance Auto Parts #103056
(Asheville, NC)
400 Merrimon Avenue
Asheville, NC 28801

Site Construction Information

Perimeter Dimensions	70' x 154'	Square Feet	10,780
Number of Roof Levels	1	Building Height	15
Perimeter Detail	🔀 Parapet Wal	I 🗌 Raised Cu	rb 🔀 Edge Metal
Wall Flashing Type	modified	Linear Feet	169
Curb Flashing Type	modified	Linear Feet	54
Edge Metal Type	painted	Linear Feet	154
Expansion Joint Type		Linear Feet	
Drainage (Drains, Scuppers,	Etc)	Gutters/conduc	tor head
Drain Overflow			
Ponding Water	🗌 Yes 🔀	No	

Roof	Assembl	y Information			
Core Cut Taken: (See work order instructions)		Moisture Present:	Yes	🗌 No	
Yes					

Mecha	nical Equipment		<u>Pe</u>	netrations	
	<u>Size</u>	<u>QTY</u>		<u>Size</u>	<u>QTY</u>
A/C Units	36" x 36"	1	Vent Pipe	2″	2
	30" x 26"	1	Soil Stack		
Refrigeration Units			Sign Supports		
			Satellite Dish		
Skylights			Electrical Conduit		
			Equipment Rails		
Other			Drains		
			Ductwork		
			Curbs	15" x 17"	4




Roof Diagram

Advance Auto Parts #103056 (Asheville, NC) 400 Merrimon Avenue, Asheville NC

09/17/2016

Customer WO: 103056

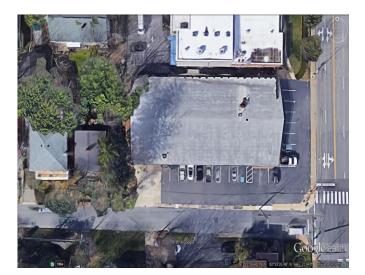

Defect 1: 25 wall flashing joints need to be cut out and re-worked.

Defect 2: remove debris from roof

Defect 3: re-broadcast ballast

Defect 4: Since we do not know the leak history – it is difficult to determine if this building should be considered for immediate re-roofing. If they are experiencing leaks other than those that may be associated with the open wall flashings – they should consider re-roofing – as it may be near the end of its service life.

Defect 5:

Defect 6:

Notes:



Phone 877-942-5613

Number of Roofs: 2 roof levels one is a small canopy

*Directions: Select one of the options for each section by marking space with an "X" for Roof 1 and 2 (if applicable)

	Roof 1	Roof 2	
	Existing Roof	Original Roof	
TYPE			
BUR	x		
MB			
Single Ply (specify type)			
DECK TYPE			
Wood			
Structural Concrete			
Metal			
Lightweight Concrete			
Other (specify)			
UNDERLAYMENT			
None			
Base Sheet			
Vapor Retarder			
Other (specify)			
INSULATION			
None			
Fiberglass			
Wood Fiber			
Polyiso			
EPS			
Other (specify)			
Number of Layers			
Attachment Method			General Condition
Total Thickness (inches)			Information
Taper (Yes or No)			

Condition Definitions:

Poor: Multiple roof assembly problems, multiple leaks, roof should be replaced within one year.

Fair: Multiple Roof assembly problems requiring extensive repairs. Corrective / Preventative work necessary.

<u>Good</u>: Some minor roof assembly problems – all repairable. A few minor leaks reported.

Excellent: No obvious / noticeable roof assembly problems. Some minor repairs may be needed, no leaks.

Survey Option Details

Moisture Survey Completed: YES XO (If yes, attach survey results)

Asbestos Test Completed: YES XO (If yes, attach asbestos test lab report)

Note: No structural analysis is included with this survey. Asbestos test or moisture test is not unless requested by customer – these services are available for an additional fee.



RECOMMENDED ACTIONS

Call 877-942-5613 for any questions.

Customer Name: Advance Auto Parts - Facilities
Site/Store Number: Advance Auto Parts #103056
(Asheville, NC)
Site Address: 400 Merrimon Avenue

Site City/State: Asheville, NC

RoofConnect WO#: 158490

Customer PO#: 103056

PLEASE COMPLETE THE FOLLOWING:

Survey Date: 9/17/2016		
Roof Type:		
Roof Size (Total sq. ft):		
Building Section:		
Roof Condition: Good	🔀 Fair	Poor

Class "C" = Corrective – inspection indicates immediate action is necessary

Class "PM" = Preventative Maintenance – inspection indicates action is necessary to extend the useful life of the roof system. Class "W" = Warranty - potential warranty claim

	Roof Defect Description	Recommended Action	Units	Class	Cost to Complete	
#	In detail describe the defect. If damaged explain how it appears to have happened.	How will repair be made?	/Qty C/PM/\		Current Year	Next Year
1	Open wall flashing joints	Cut out existing areas weld 15" modified patches	25		\$	\$
2	Debris on roof	Remove debris on roof			\$	\$
3	Ballast missing in areas	Re-broadcast ballast	50 sf		\$	\$
4					\$	\$
Tot	al All Recommended Actions				\$	\$
LAB	52 hours (2 techs) @ \$89.00 30R				\$4,628.00	\$
Ma	Modified membrane terial				\$598.00	\$
Ma	terial				\$	\$
Ma	terial				\$	\$
Ma	terial				\$	\$
Ma	terial				\$	\$
ТАХ	A TAX AS Applicable				\$	\$
	tal All Recommended Actions			1	\$5,226.00	\$

Pricing may vary if all recommended actions are not approved. Pricing valid for 30 days from date of survey.

WO#40532_Advance_AutoAsheville_002.jpg WORKORDER:[WO #158490 (ALT#:40532) (CL#:103056)] OVErViEW	
WO#40532_Advance_AutoAsheville_003.jpg WORKORDER:[WO #158490 (ALT#:40532) (CL#:103056)] OVErvieW	
WO#40532_Advance_AutoAsheville_004.jpg WORKORDER:[WO #158490 (ALT#:40532) (CL#:103056)] OVErVIEW	

WO#40532_Advance_AutoAsheville_005.jpg WORKORDER:[WO #158490 (ALT#:40532) (CL#:103056)] typical penetration	
WO#40532_Advance_AutoAsheville_006.jpg WORKORDER:[WO #158490 (ALT#:40532) (CL#:103056)] repair area - re=broadcast ballast to this area	
WO#40532_Advance_AutoAsheville_007.jpg WORKORDER:[WO #158490 (ALT#:40532) (CL#:103056)] typical wall flashing	

W0#40532_Advance_AutoAsheville_008.jpg WORKORDER:[WO #158490 (ALT#:40532) (CL#:103056)] open wall flashing joints	
WO#40532_Advance_AutoAsheville_009.jpg WORKORDER:[WO #158490 (ALT#:40532) (CL#:103056)] open wall flashing joints	
WO#40532_Advance_AutoAsheville_010.jpg WORKORDER:[WO #158490 (ALT#:40532) (CL#:103056)] open wall flashing joints	

WO#40532_Advance_AutoAsheville_011.jpg WORKORDER:[WO #158490 (ALT#:40532) (CL#:103056)]	
open wall flashing joints	
WO#40532_Advance_AutoAsheville_017.jpg WORKORDER:[WO #158490 (ALT#:40532) (CL#:103056)]	
open wall flashing joints	
WO#40532_Advance_AutoAsheville_022.jpg WORKORDER:[WO #158490 (ALT#:40532) (CL#:103056)] typical penetrations	

